

**ENVIRONMENTAL COMPLIANCE & AREA COMPLETION PROJECTS (EC&ACP) STANDARD
OPERATING PROCEDURES, VOL. I**
Manual: C3
Procedure: ER-IDS-019-050
Revision: 4
Effective Date: 01/18/2022
Type-Class: Checklist
Page: 1 of 3
**M-AREA INACTIVE PROCESS SEWER LINE (MIPSL) OPERABLE UNIT 081-M FIELD INSPECTION
CHECKLIST**
WORKING COPY

This document is a Working Copy. Prior to start of work, verify this is the latest revision per the Procedure Index.

Dylan Price
Verified By

12-20-24
Date

CAUTION

The Inspector is required to IMMEDIATELY notify the Post-Closure Manager and Environmental Compliance Authority if there has been a breach or compromise of the institutional controls of this waste unit. This notification is required to be in accordance with Savannah River Site post-closure inspection procedures.

NOTE

1. Manual C3, Volume 1, Procedure ER-SOP-019, Waste Unit and IOU Inspection and Maintenance, is referenced for inspection details.
2. Steps in this checklist may be completed concurrently or in any order.

 SCHEDULED

 UNSCHEDULED

A = Satisfactory X = Unsatisfactory (Explanation required)		A or X	Observation/Corrective Action Taken
1.	VERIFY roads are accessible.	A	
2.	VERIFY waste unit signs (9) are in acceptable condition, have correct information, and are legible from a distance of 25 feet.	A	

M-Area Inactive Process Sewer Line (MIPSL) Operable Unit 081-M Field Inspection Checklist

Manual: C3
 Procedure: ER-IDS-019-050
 Revision: 4
 Page: 2 of 3

SCHEDULED


UNSCHEDULED

A = Satisfactory		A or X	Observation/Corrective Action Taken
X = Unsatisfactory (Explanation required)			
3.	INSPECT waste unit for erosion, abnormal soil cracks, depressions, and burrowing animals.	A	
4.	VERIFY there are no excavation, digging, construction activities over underground sewer lines, at sewer outlet, at A-014 Outfall, or at the manholes.	A	
5.	VERIFY pipelines and manhole plugs are intact.	A	
6.	CHECK survey unit boundary markers for damage and visibility.	A	
7.	Other.	A	

Inspected By		
Dylan Price (Print Name)	Dylan Price (Signature)	12-20-24 (Date)

Reviewed By Post-Closure Manager		
BRIAN HANSGEW (Print Name)	BHG (Signature)	1-2-2025 (Date)

M-AREA INACTIVE PROCESS SEWER LINE (MIPSL) OPERABLE UNIT 081-M

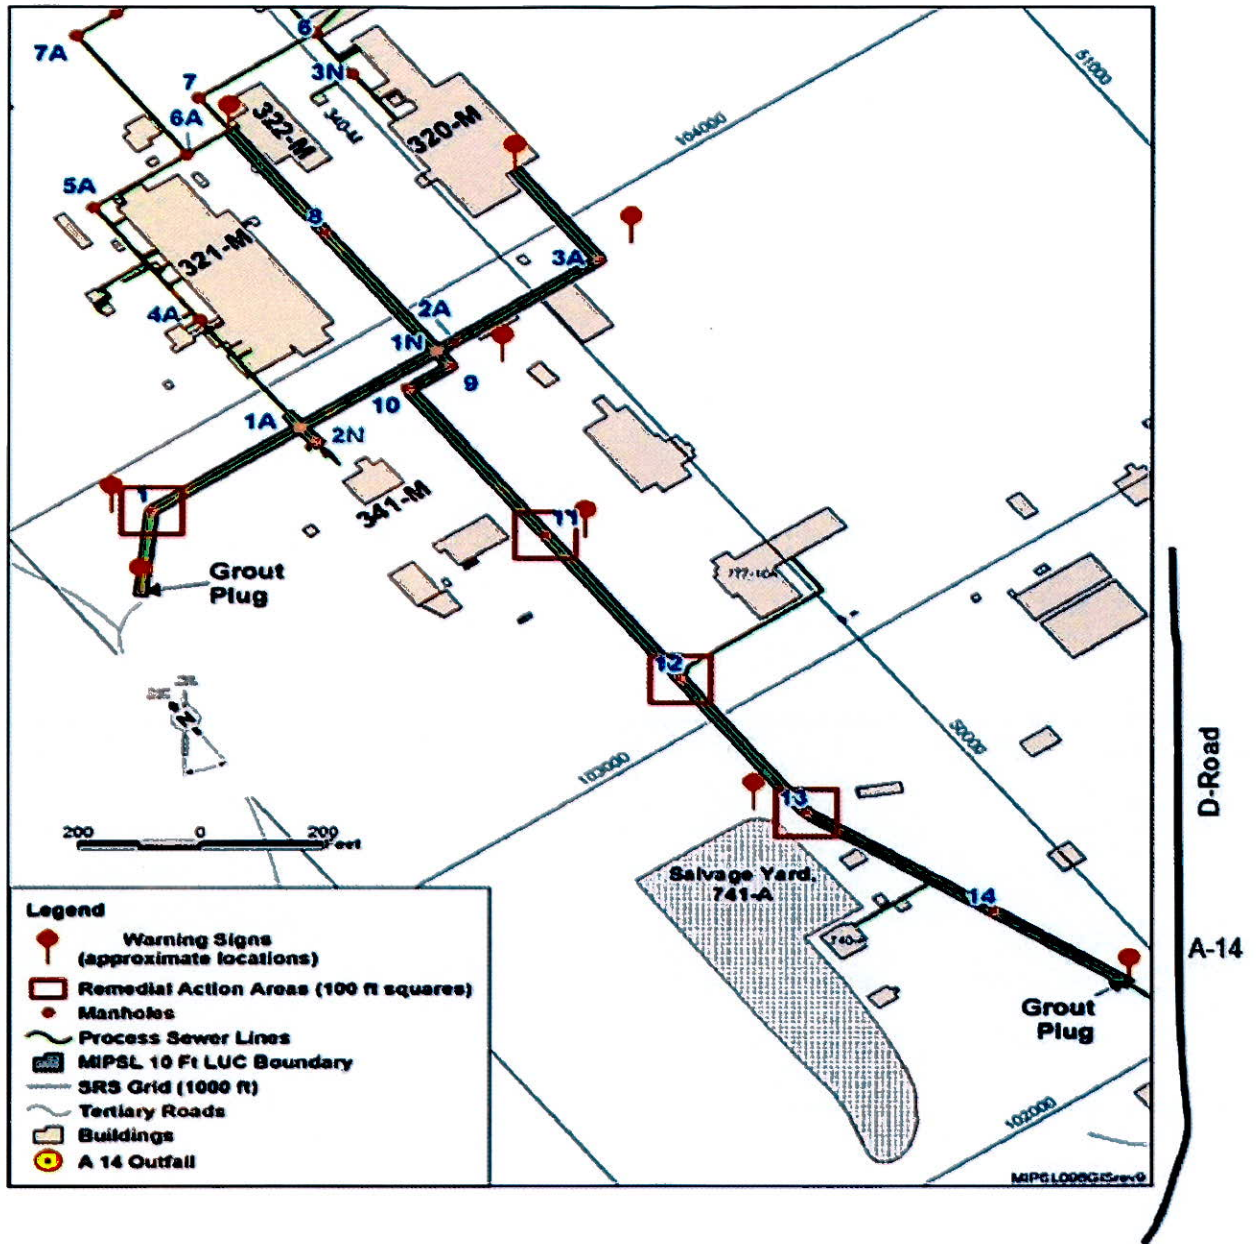

NOTES: None
