


**ENVIRONMENTAL COMPLIANCE & AREA COMPLETION PROJECTS (EC&ACP) STANDARD  
OPERATING PROCEDURES, VOL. I**
**Manual: C3**  
**Procedure: ER-IDS-019-050**  
**Revision: 4**  
**Effective Date: 01/18/2022**  
**Type-Class: Checklist**  
**Page: 1 of 3**
**M-AREA INACTIVE PROCESS SEWER LINE (MIPSL) OPERABLE UNIT 081-M FIELD INSPECTION  
CHECKLIST**
**WORKING COPY**

This document is a Working Copy. Prior to start of work, verify this is the latest revision per the Procedure Index.

  
Verified By

9/24/2024  
Date

**CAUTION**

The Inspector is required to IMMEDIATELY notify the Post-Closure Manager and Environmental Compliance Authority if there has been a breach or compromise of the institutional controls of this waste unit. This notification is required to be in accordance with Savannah River Site post-closure inspection procedures.

**NOTE**

1. Manual C3, Volume 1, Procedure ER-SOP-019, Waste Unit and IOU Inspection and Maintenance, is referenced for inspection details.
2. Steps in this checklist may be completed concurrently or in any order.

 **SCHEDULED**
 **UNSCHEDULED**

A = Satisfactory		A or X	Observation/Corrective Action Taken
X = Unsatisfactory (Explanation required)			
1.	VERIFY roads are accessible.	A	
2.	VERIFY waste unit signs (9) are in acceptable condition, have correct information, and are legible from a distance of 25 feet.	A	

## M-Area Inactive Process Sewer Line (MIPSL) Operable Unit 081-M Field Inspection Checklist

Manual: C3  
 Procedure: ER-IDS-019-050  
 Revision: 4  
 Page: 2 of 3

 SCHEDULED


 UNSCHEDULED

A = Satisfactory		A or X	Observation/Corrective Action Taken
X = Unsatisfactory (Explanation required)			
3.	INSPECT waste unit for erosion, abnormal soil cracks, depressions, and burrowing animals.	A	
4.	VERIFY there are no excavation, digging, construction activities over underground sewer lines, at sewer outlet, at A-014 Outfall, or at the manholes.	A	
5.	VERIFY pipelines and manhole plugs are intact.	A	
6.	CHECK survey unit boundary markers for damage and visibility.	A	
7.	Other. None	A	

## Inspected By

Douglas Barron (Print Name)	 (Signature)	9/24/2024 (Date)
--------------------------------	---	---------------------


## Reviewed By Post-Closure Manager

Brian Hanshew (Print Name)	 (Signature)	10/9/2024 (Date)
-------------------------------	---	---------------------

M-Area Inactive Process Sewer Line (MIPSL) Operable Unit  
081-M Field Inspection Checklist

Manual: C3  
Procedure: ER-IDS-019-050  
Revision: 4  
Page: 3 of 3

M-AREA INACTIVE PROCESS SEWER LINE (MIPSL) OPERABLE UNIT 081-M

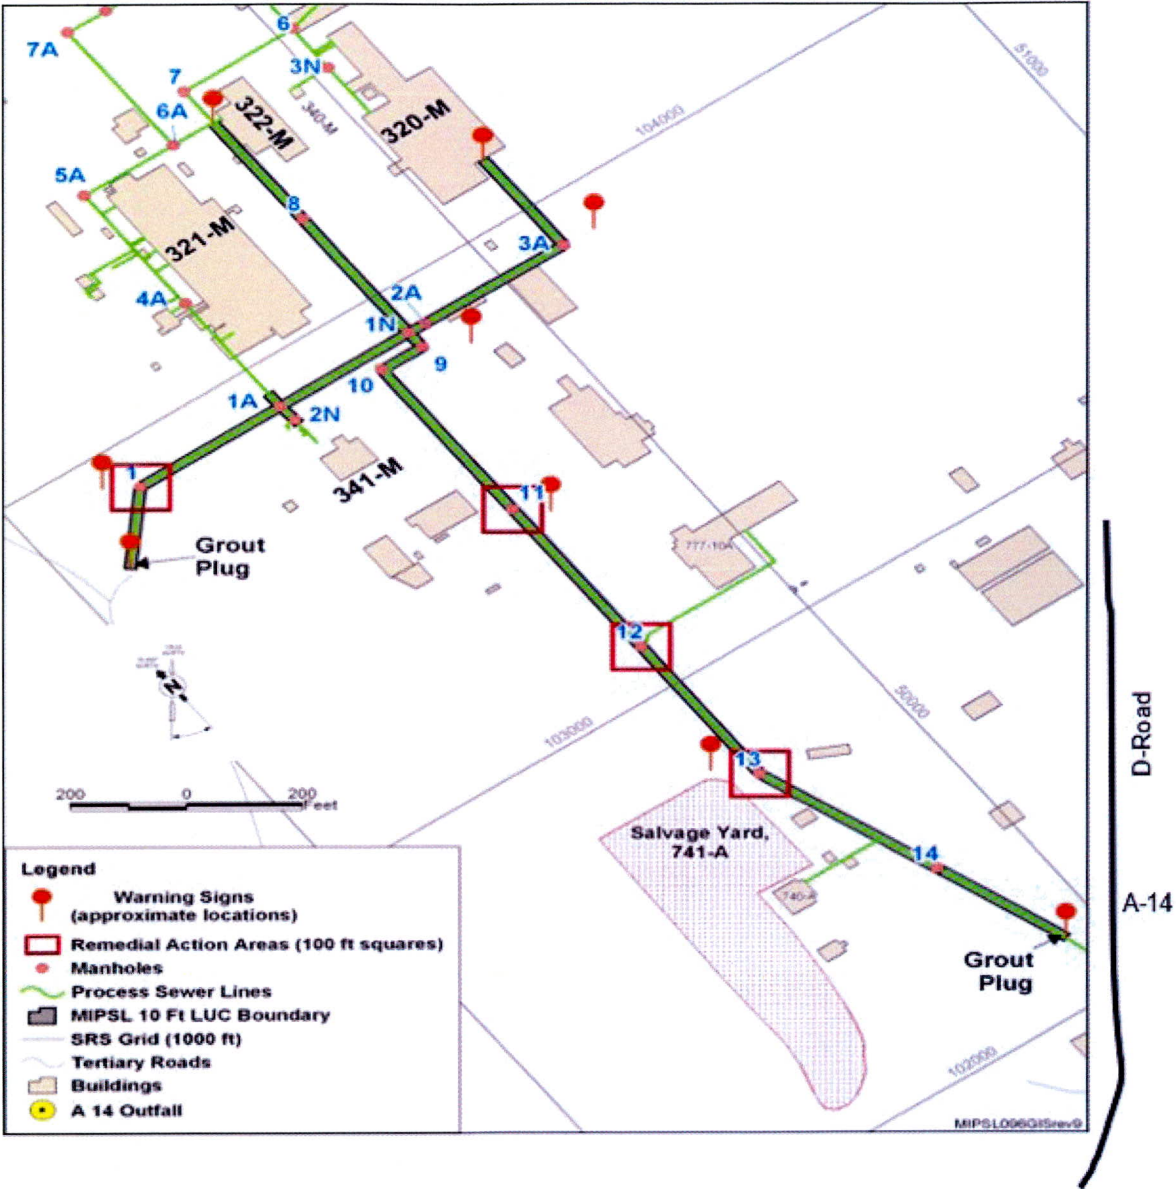

NOTES: None

---

---

---

---

---
