OPERATION AND MAINTENANCE ACTIVITY PLAN

221-F Fire Water Leak Repair Project

Prepared by : DONALD K PARKMAN FOR H.N. GOTSCH PER EMAIL — 7-16-2020
H.N. Gotsch, F-Area Operation ECA — Date

Approved by : DONALD K PARKMAN FOR C.J. WARD PER EMAIL — 7-16-2020
C.J. Ward, Operational Compliance Manager — Date

Approved by: — 7-16-2020
D.K Parkman, FAC Ops Support Manager — Date

Approved by: — 7/16/20
W.E. Minton, RPD FLM — Date

1. INTRODUCTION

This Operation and Maintenance (O&M) Plan is being written to support work activities planned to replace the defective line fitting for a fire water leak near the 221-F as shown in Figure 1 with the Site Evaluation Areas identified in red (Reference 1) and Figure 2. This O&M Plan is characterized as "minor intrusive" because there's no planned excavation activities of the RCRA/CERCLA area(s).

Figure 1

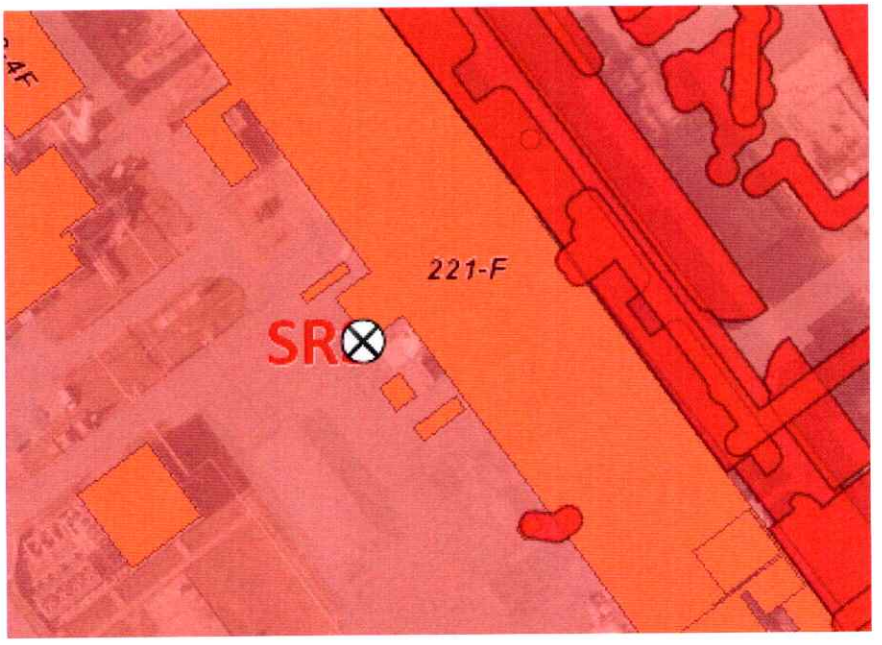


Figure 2



2. AREA DESCRIPTION AND CONDITIONS

Site Evaluation Areas exist within 200 feet of this work location and include the following contaminants:

1. Waste Unit ID 343, Sandblast Area CMF-001
   Location: East of 221-F (A-line & 211-F)
   Contaminants: Lead and chromium

2. Waste Unit ID 394, Spill on 2/25/85 of 20,000CM of Water Vapor-Rad
   Location: 221-F

3. Waste Unit ID 563, F-Area Process Sewer Lines as Abandoned.
   Location: F-Area
   Contaminants: Unknown alpha, beta, gamma, and metals

4. Waste Unit ID 575, General Separations Area Western Groundwater Operable Unit
   Location: F-Area

5. SPF-006, 292-1F Vessel Vent Fan work, 11/1/57
   Location: 800 sq feet around 292-1F, North and East of 221-F and North of 292-F
   Contaminants: Unknown beta-gamma

6. SPF-010, Spill on 1/1/58 of Unknown Quantity of High Level Waste
   Location: 221-F Section 9 Head Tower
   Contaminants: Sr-90, Cs-137

A site evaluation has not been performed and impacts to the IOU have not been determined.

3. O & M ACTIVITY

A. O&M Activity Description

The O&M activity involves fire water leak repair outside facilities near Section 9 of 221-F. Every attempt should be made to place any soil removed from the excavation site back into the hole.

If any soil cannot be placed back into its original hole it will be screened by RCO for free release to the 3 Rivers Landfill.

a. If the excess soil is below radiological limits and can be cleared for release to the 3 Rivers Landfill it shall be placed into an appropriate container and shipped accordingly.
b. If the soil cannot be cleared for release to the 3 Rivers Land Fill it will be placed into one or more containers to be specified by the facility GCO. It shall be sampled for constituents to be determined by the F-Area ECA and/or Waste CTF. The containers will be held pending analysis and waste characterization.

B. O&M Activity Sampling and Monitoring for Health and Safety

The work area will be barricaded with rope or rigid handrail to ensure that access is controlled. This is due to personnel safety around the work area.

Worker health and safety will be directed and controlled as required in the work package and the Assisted Hazard Analysis (AHA).

RPD will monitor the water and/or soil removal activities for radioactive contamination per their standard procedures. If radiological contamination is encountered RPD will determine if protective equipment and personnel access restrictions are required.

C. Health and Safety Plan

The health and safety concerns involve worker exposure to contaminants of interest listed in Section 2 above.

The Work Order and/or AHA for these activities will contain instructions to comply with this plan.

The safety requirements and personal protective equipment described in these documents is appropriate for the potential hazards of the waste units.

D. Characterization and Sampling Plan for the Affected Area within the Unit

The Soil Sampling Plan outlines the ongoing sampling/analysis. If soil is to be removed from this area, it will be sampled by RCO personnel. These samples will be analyzed to allow the soil to be cleared for release to the 3 Rivers Landfill. If the excess soil cannot be cleared for release it will be sampled for waste characterization and planning for that will occur when that determination is made. The F-Area Waste ECA and/or Waste CTF will provide specific analytical requirements for that material.

Additional work scope and sampling from the soil disturbance areas or water removal activities may be necessary and will be addressed per guidance from the Facility Manager (FM) or designee, RPD and the SRS SRNS-OSC (On-Scene Coordinator) should radioactive contamination outside the identified area be found present.

E. Contaminated Materials Management and/or Disposal

The disposal of the waste materials generated during this activity will be contingent upon the survey results. Other clean waste originating from this job will be managed as appropriate and specified by RCO, or handled in accordance with existing F –Area procedures.

If radioactive contamination is found, the ECA and/or GCO will be contacted before any soil is placed into a container for disposal. Any other job control waste will be disposed of as "Low Level Radioactive Waste" under current F-Area Waste Management procedures if deemed appropriate by the SRNS-OSC.

F. Environmental Plans and Permit Modification Requests:

No permit modifications are required as a result of this activity.

4. CONTINGENCY PLAN

If at any time during the implementation of the activity, the conditions change such that the activity is no longer considered "minor" (as defined in Reference 1) or any other unanticipated event occurs, the Project Manager or Environmental Compliance Authority shall:

- Immediately notify the SRNS-OSC. The SRNS-OSC will notify the DOE-OSC
- Contain and stabilize the area, investigate as necessary to determine the necessary change in the activity plan, secure the area, and stop work.
- Update the SRNS-OSC as to the findings and the requested path forward. The SRNS-OSC will communicate the information to the DOE-OSC and obtain concurrence on the path forward

5. DOCUMENTATION & REPORTING

The Project Manager will transmit the following documentation to the SRNS-OSC by the 31st day of the month the activity was completed:

- the signed O&M plan
- Any sampling and characterization data collected,
- Quantity of contaminated materials generated, and
- Treatment, storage, and disposal location of contaminated material

6. References

1. WSRC-RP-96-45, Savannah River Site Plan for Performing Maintenance in Federal Facility Agreement Area (O&M) Plan (U), December 15, 1996
