ENVIRONMENTAL COMPLIANCE & AREA COMPLETION PROJECTS

Baseline Asbestos Inspection Report of Building 701-4F



Q-APG-F-00424
June 6, 2024

Savannah River
NUCLEAR SOLUTIONS℠
FLUOR • NEWPORT NEWS NUCLEAR • HONEYWELL

INTEROFFICE MEMORANDUM

Q-APG-F-00424
RSM Track Number 10755

June 6, 2024

TO: Patrick O'Neill, 730-4B

FROM: James Moore, 730-4B

BASELINE ASBESTOS INSPECTION REPORT OF BUILDING 701-4F

On May 22, 2024, an inspection was performed to determine the presence of any Asbestos Containing Material (ACM) in building 701-4F. Constructed circa 1988, 701-4F is a single-story building comprised of a reinforced steel framework, concrete, and Concrete Masonry Unit (CMU) blocks. The building is supported by a concrete slab foundation with a footprint of approximately 2,000 square feet. The CMU block wall exterior is finished with a polystyrene and stucco façade. The current roofing system is comprised of mechanically attached polyisocyanurate board and reinforced thermoplastic membrane. Building 701-4F was utilized as security access point to enter F-Area Material Storage area inside the fenced.

Ten (10) homogenous types of material were evaluated during this inspection. Most of the evaluated suspect materials were sampled and analyzed in previous asbestos inspections. Please see the attached Inspection Survey Table for descriptions, estimated quantities, results, and locations of the materials inspected. The analytical results from the previous reports have been reproduced and are included in the Inspection Survey Table. This asbestos inspection report will serve as an ACM baseline and reference to support any various scopes of work involving renovations/repairs to the building.

SUMMARY

All accessible, visible, suspect ACM was evaluated at the time of this inspection. Fiberglass (domestic water, HVAC ductwork) and elastomeric foam (roof drain line and condensing lines) were the only visible Thermal System Insulation (TSI) identified during the completion of this inspection. These types of insulation do not contain asbestos. This evaluation was based on facility knowledge, material knowledge, document review, visual inspection, tactile inspection, and bulk sample analyses. **Asbestos trained personnel, with proper permitting, and waste disposal must be utilized if ACM or Presumed Asbestos Containing Material (PACM) is removed or disturbed.**

The electrical wiring insulation and electrical panel boxes were not included in this inspection. Therefore, all suspect materials (if any) inside the electrical panel boxes and conduit are considered Presumed Asbestos Containing Material (PACM) until evaluated by a licensed asbestos inspector. The roof has a white membrane with insulation underneath but still needs to be tested before it's removed or replaced. In addition, all suspect gaskets (if any) must be handled as PACM unless documentation exists or determined otherwise by a licensed asbestos inspector.

In accordance with 40CFR part 61.145 a **ten-day notification** must be filed with SC DHEC prior to demolition. Properly trained personnel, a demo permit, and proper waste disposal will be required.

Savannah River
NUCLEAR SOLUTIONS℠
FLUOR • NEWPORT NEWS NUCLEAR • HONEYWELL

INTEROFFICE MEMORANDUM

Q-APG-F-00424
RSM Track Number 10755

All samples were analyzed by Polarized Light Microscopy (PLM). The South Carolina Department of Health and Environmental Control (SCDHEC) Regulation 61-86.1 requires additional Transmission Electron Microscopy (TEM) on organically bound samples to confirm negative PLM results. Samples collected in prior to 2006 were analyzed at the WSRC Industrial Hygiene Laboratory, accredited by the American Industrial Hygiene Association (AIHA) Laboratory Quality Assurance Program (LQAP) in the Field of Testing (FoT)/PLM. The laboratory ID number is #3100642. The analysts have attended Course 1608A: Microscopical Identification of Asbestos, presented by McCrone Research Institute or equivalent.

Samples collected in prior to 2006 were analyzed at the WSRC Industrial Hygiene Laboratory, accredited by the American Industrial Hygiene Association (AIHA) Laboratory Quality Assurance Program (LQAP) in the Field of Testing (FoT)/PLM. The laboratory ID number is #3100642. The analysts have attended Course 1608A: Microscopical Identification of Asbestos, presented by McCrone Research Institute or equivalent.

All other collected samples were analyzed by R J Lee Group, Inc. The laboratory is located at 800 Presque Isle Drive, Suite 300 Pittsburgh, PA 15239. Please see the attached laboratory report for a review of accreditations and certifications.

ASBESTOS INSPECTOR	INSTITUTION	CERT. NO.	STATE	EXP. DATE
James Moore	Greenville Tech College	242-EVT502-062	SC	**04/18/2025**
	Included on the SRS Long-term in-house Group license ABS 8021			

ASBESTOS INSPECTOR	INSTITUTION	CERT. NO.	STATE	EXP. DATE
Carlos Santos	Greenville Tech College	242-EVT502-064	SC	**04/18/2025**
	Included on the SRS Long-term in-house Group license ABS 8021			


Daxton Holjes, 730-4B
William Padgett, 730-4B
C: C.R.F., 773-52A
Site D&D Correspondence File

INSPECTION SURVEY TABLE OF BUILDING 701-4F

Homogeneous Number	Suspect/ Non-Suspect Material	Description and Sample Numbers of Material	Estimated Amount	Test Results	Friable/ Non-friable Condition
Asbestos Containing Material					
H02OA H02OB	Miscellaneous	**Description:** 12x12 Tan/white speck floor tile & Mastic **Sample Numbers:** 7014F060213–03, 7014F060213–04, 7014F060213–09, 7014F060213–10, 7014F060213–17, 7014F060213–18, **Sample Number:** 7014F240522-01A analyzed via TEM	~1,300 Square Feet	**Positive**	Non-friable Good Condition
Location: Interior: On the floor under tile (computer room has no floor covering) inseparable tile and mastic material					
Non-Asbestos Material					
H03OB	Miscellaneous	**Description:** Adhesive on 3" cove base molding **Sample Numbers:** 7014F060213–05, 7014F060213–11 **Sample Number:** 7014F240522-03A analyzed via TEM			Negative
Location: Interior: at the base of the walls					
H04OB	Miscellaneous	**Description:** White putty **Sample Numbers:** 7014F060213–06, 7014F060213–14, **Sample Number:** 7014F240522-04A analyzed via TEM			Negative
Location: Interior: at the expansion joints, corners, and around entrance doors					
H05OB	Miscellaneous	**Description:** 2'x 2' white perforated ceiling tiles **Sample Numbers:** 7014F060213–07, 7014F060213–12, 7014F060213–19			Negative
Location: Main ceiling tile					
H06OB	Miscellaneous	**Description:** 2'x 2' white perforated ceiling tiles **Sample Numbers:** 7014F060213–08, 7014F060213–13, 7014F060213–20			Negative
Location: Replacement ceiling tile					

INSPECTION SURVEY TABLE OF BUILDING 701-4F


H07OB	Miscellaneous	**Description:** Red penetration putty **Sample Numbers:** 7014F060213–15, 7014F060213–16 **Sample Number:** 7014F240522-05A analyzed via TEM	Negative
Location: Interior: overhead on the west wall of the computer room			
H08	Miscellaneous	**Description:** Black cloth inside of pre-insulated duct **Sample Numbers:** 7014F060214–01, 7014F060214–02	Negative
Location: Inside duct			
H09OB	Miscellaneous	**Description:** Blue putty **Sample Numbers:** 7014F060214–03, 7014F060214–04, **Sample Number:** 7014F240522-06A analyzed via TEM	Negative
Location: Interior: On the north wall in ceiling in the hallway by room 108			
H10OB	Miscellaneous	**Description:** Gypsum board above ceiling tile **Sample Number:** 7014F240522-07, 7014F240522-08, 7014F240522-09	Negative
Location: Eastside of the building above the 2nd door entering the building			
H01OB	Miscellaneous	**Description:** White elastomer **Sample Number:** 7014F060213–01, 7014F060213–02 **Sample Number:** 7014F240522-01A analyzed via TEM	Negative
Location: Exterior: at the expansion joints, corners, and around entrance doors			

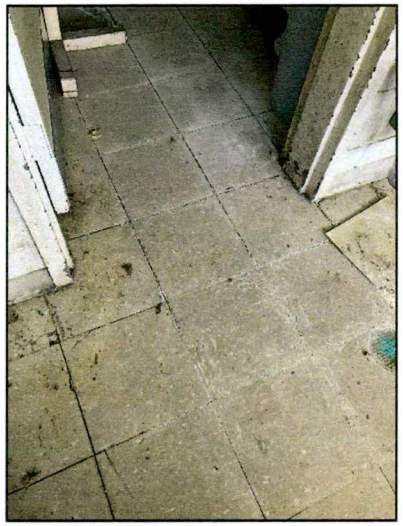

Floor




Fiberglass insulation

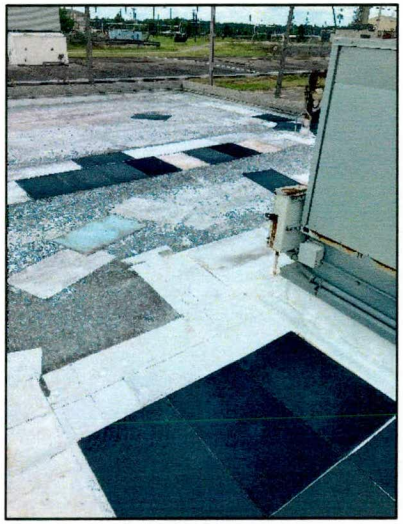

Roof



Ceiling tiles

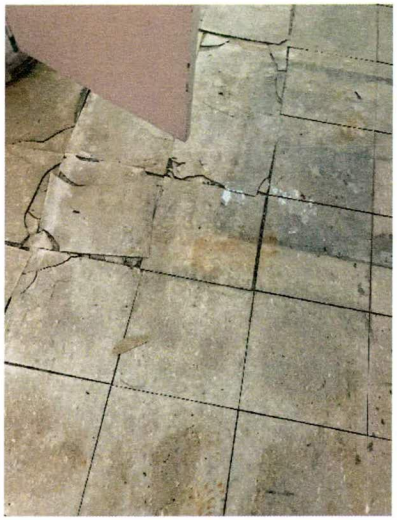

Floor

OSR 4-434 (Rev 3-15-2004)

Industrial Hygiene Chain of Custody Lab Report

Westinghouse Savannah River Company
Industrial Hygiene Laboratory
Building 735-B, Room 310
Aiken, SC 29808
Phone: (803) 952-7449/7459
Fax: (803) 952-7881

Page 1 of 3

Lab Log-In No.

Contaminant(s): SUSPECT ASBESTOS (701-4F)

Lab Report No.: EBL-IH 2006-0108

Lab Method No. and Name: 18 PLM

Lab Book and Page No.: 35 599-603

Disk No.:

Submitted By (Print/Signature): Steve Ledbetter

Verbal Results Given (To Whom):

How (Check One): O Person C Voice Mail

Audited By (Print/Signature): Scott Self SAS

Date/Time Verbal Results Given:

Sample ID	Sample Media/Size	Requested TAT*	Results/Unit	LOD/Units	Remarks
7014F060213-01		02/27/06	< 1 %	Asbestos 1%	H01-White elastamer - Exterior walls
7014F060213-02		02/27/06	< 1%		H01-White elastamer - Exterior walls
7014F060213-03		02/27/06	< 1%		H02A-12x12 tan/white speck floor tile - Int
7014F060213-04		02/27/06	per Chrys 5-15%		H02B-Mastic/12x12 tan/white speck fl tile
7014F060213-05		02/27/06	< 1%		H03-Adhesive on cove base - Interior walls
7014F060213-06		02/27/06	< 1%		H04-White putty - interior door frames
7014F060213-07		02/27/06	< 1%		H05-White perforarted ceiling tile - Int
7014F060213-08		02/27/06	< 1%		H06-White design ceiling tile - interior
7014F060213-09		02/27/06	< 1%		H02-12x12 tan/white speck floor tile - Int

Analyst/Signature	Date Analyzed	Reviewed By (Print)	Signature (Lab Director or Designee)	Date
RN Bostt	2/23/06	M Bernard	Maureen Bernard	2-23-06
Analyst/Signature	Date Report Mailed	Report Received By (Print)	Signature (Field Use Only)	Date Received
RN Bostt	2/23/06			

Comments
Activity Code: UD131PLAT

Chain of Custody

NOTE: Samples from Radiological Contamination areas must meet free release criteria.

Relinquished By				Received By			
Name	Signature	Date	Time	Name	Signature	Date	Time
Steve Ledbetter		2/13/2006		RM Cooke	RM Cooke	2/13/06	1630

*TAT - Turn Around Time Disk No. - Only applicable to asbestos fiber counting

Retention - Permanent

OSR 4-434 (Rev 3-15-2004)

Industrial Hygiene Chain of Custody Lab Report

Westinghouse Savannah River Company
Industrial Hygiene Laboratory
Building 735-B, Room 310
Aiken, SC 29808
Phone: (803) 952-7449/7459
Fax: (803) 952-7881

Lab Log-In No. _____ Page 2 of 3

Contaminant(s): SUSPECT ASBESTOS (701-4F)

Lab Report No.: EBL-IH 2006-0108

Lab Method No. and Name: 18 PLM

Lab Book and Page No.: 35 599-603

Disk No.:

Submitted By (Print/Signature): Steve Ledbetter

Verbal Results Given (To Whom):

How (Check One): ○ Person ○ Voice Mail

Audited By (Print/Signature): Scott Self SAS

Date/Time Verbal Results Given:

Sample ID	Sample Media/Size	Requested TAT*	Results/Unit	LOD/Units	Remarks
7014F060213-10		02/27/06	Pos Chrys 5-15%	Asbestos 1%	H02B-Mastic/12x12 tan/white speck fl tile
7014F060213-11		02/27/00	< 1%		H03-Adhesive on cove base - Interior walls
7014F060213-12		02/27/06	< 1%		H05-White perforarted ceiling tile - Int
7014F060213-13		02/27/06	< 1%		H06-White design ceiling tile - interior
7014F060213-14		02/27/06	< 1%		H04-White putty - interior door frames
7014F060213-15		02/27/06	< 1%		H09-Red putty - computer rm - west int wall
7014F060213-16		02/27/06	< 1%		H09-Red putty - computer rm - west int wa
7014F060213-17		02/27/06	< 1%		H02-12x12 tan/white speck floor tile - Int
7014F060213-18		02/27/06	Pos Chrys 5-15%		H02B-Mastic/12x12 tan/white speck fl tile

Analyst/Signature	Date Analyzed	Reviewed By (Print)	Signature (Lab Director or Designee)	Date
RN Scott	2/23/06	M Bernard	Maureen Bernard	2/23/06
Analyst/Signature	Date Report Mailed	Report Received By (Print)	Signature (Field Use Only)	Date Received
RN Scott	2/23/06			

Comments
Activity Code: UD131PLAT

Chain of Custody

NOTE: Samples from Radiological Contamination areas must meet free release criteria.

Relinquished By				Received By			
Name	Signature	Date	Time	Name	Signature	Date	Time
Steve Ledbetter		2/13/2006		PM Cooke	PM Cooke	2/13/06	1630

*TAT - Turn Around Time Disk No. - Only applicable to asbestos fiber counting.
Retention - Permanent

OSR 4-434 (Rev 3-15-2004)

Industrial Hygiene Chain of Custody Lab Report

Westinghouse Savannah River Company
Industrial Hygiene Laboratory
Building 735-B, Room 310
Aiken, SC 29808
Phone: (803) 952-7449/7459
Fax: (803) 952-7881

Lab Log-In No. _____ Page 3 of 3

Contaminant(s)	Lab Report No.	Lab Method No. and Name
SUSPECT ASBESTOS (701-4F)	EBL-IH 2006-0108	18 PLM
		Lab Book and Page No.: 35 599-603 / Disk No.
Submitted By (Print/Signature): Steve Ledbetter		Verbal Results Given (To Whom) / How (Check One): ○ Person ○ Voice Mail
Audited By (Print/Signature): Scott Self SA		Date/Time Verbal Results Given

Sample ID	Sample Media/Size	Requested TAT*	Results/Unit	LOD/Units	Remarks
7014F060213-19		02/27/06	< 1%	Asbestos 1%	H05-White perforarted ceiling tile - Int
7014F060213-20		02/27/06	< 1%	↓	H06-White design ceiling tile - interior

Analyst/Signature	Date Analyzed	Reviewed By (Print)	Signature (Lab Director or Designee)	Date
RN Scott	2/23/06	M Bernard	J Maureen Bernard	2/23/06
Analyst/Signature	Date Report Mailed	Report Received By (Print)	Signature (Field Use Only)	Date Received
RN Scott	2/23/06			

Comments
Activity Code: UD131PLAT

Chain of Custody

NOTE: Samples from Radiological Contamination areas must meet free release criteria.

Relinquished By				Received By			
Name	Signature	Date	Time	Name	Signature	Date	Time
Steve Ledbetter	Steve Ledbetter	2/13/2006		RM Cooke	RM Cooke	2/13/06	1630

*TAT - Turn Around Time Disk No. - Only applicable to asbestos fiber counting.

Retention - Permanent

OSR 4-434 (Rev 3-15-2004)

Industrial Hygiene Chain of Custody Lab Report

Westinghouse Savannah River Company
Industrial Hygiene Laboratory
Building 735-B, Room 310
Aiken, SC 29808
Phone: (803) 952-7449/7459
Fax: (803) 952-7881

Lab Log-In No. _____ Page 1 of 1

Contaminant(s): SUSPECT ASBESTOS (701-4F)	Lab Report No. EBLJH 2006-0116	Lab Method No. and Name: K PLM	
		Lab Book and Page No.: 35 605	Disk No.
Submitted By (Print/Signature): Steve Ledbetter		Verbal Results Given (To Whom)	How (Check One): O Person O Voice Mail
Audited By (Print/Signature): Scott Self SAS		Date/Time Verbal Results Given	

Sample ID	Sample Media/Size	Requested TAT*	Results/Unit	LOD/Units	Remarks
7014F060214-01		02/28/06	< 1%	1% asbestos	H16-Black cloth inside duct -over Rm 108
7014F060214-02		02/28/06	< 1%	↓	H16-Black cloth inside duct -over Rm 108
7014F060214-03		02/28/06	< 1%		H16-Blue putty - North wall over Rm 108
7014F060214-04		02/28/06	< 1%		H16-Blue putty - North wall over Rm 108

Analyst/Signature: RM Cooke	Date Analyzed: 2/25/06	Reviewed By (Print): M Bernard	Signature (Lab Director or Designee): Maureen Bernard	Date: 2/27/06
Analyst/Signature: RM Cooke	Date Report Mailed: 2/27/06	Report Received By (Print)	Signature (Field Use Only)	Date Received

Comments
Activity code: UD131PLAT

Chain of Custody

NOTE: Samples from Radiological Contamination areas must meet free release criteria.

Relinquished By				Received By			
Name	Signature	Date	Time	Name	Signature	Date	Time
Scott Self	SAS	2/14/2006		R N GANTT	R N Gantt	2/15/06	

*TAT - Turn Around Time Disk No. - Only applicable to asbestos fiber counting.
Retention - Permanent

RJ LEE GROUP
DELIVERING SCIENTIFIC RESOLUTION

Laboratory Report

RJ Lee Group Inc.
800 Presque Isle Dr, Pittsburgh, PA 15239-2799
Tel: 724-325-1776 | Fax: 724-733-1799

Savannah River Nuclear Solutions US DOE
SRNS LLC
Aiken, SC 29808
US
Attention: William Padgett
Telephone: 803-952-5650

Report Date	06/06/2024 08:46:57
Sample Receipt Date	05/28/2024 11:55:58
RJ Lee Group Job No.	COH1074798
Authorization/P.O. No.	Subcontract 996
Client Job No./Name	7014F240522

Method: EPA/600/R-93/116

RJLG Sample Number	Client Sample Number	Homogeneous	# of Layers	Asbestos Detected(%)	Non-Asbestos Fibers(%)	Non-Fibrous Materials(%)	Matrix Material	Analyst-Analysis Date
10618298	7014F240522-07	No	2	ND	23.20%	76.80%	Carbonates, Gypsum, Misc. Particles	AD - 06/04/2024
					Cellulose			
Label: 06/04/2024 10:40								
Description: Beige and white rocky material, black and brown paper material								
Layer Information:								
	85%-Beige and white rocky material	Yes		ND	10.00%	90.00%	Carbonates, Gypsum	
					Cellulose			
	15%-Brown and black paper material	Yes		ND	98.00%	2.00%	Misc. Particles	
					Cellulose			
10618299	7014F240522-08	No	2	ND	9.75%	90.25%	Carbonates, Gypsum	AD - 06/04/2024
Label: 06/04/2024 10:40					Cellulose			
Description: White and beige rocky material, brown and black paper material								
Layer Information:								
	95%-White and beige rocky material	Yes		ND	5.00%	95.00%	Carbonates, Gypsum	
					Cellulose			
	5%-Brown and black paper	Yes		ND	100.00%			

DISCLAIMER NOTES
1. "ND" indicates no asbestos was detected.
2. "Trace" or "<" indicates asbestos was identified in the sample, but the concentration is less than the method quantitation limit.
PLM coefficients of variance range from approximately 1.8 at the quantitation limit of 0.25% to 0.32 at high fiber concentrations.
3. Sample(s) for this project were analyzed at our: Pittsburgh, PA (AIHA LAP, LLC. #292885, NY ELAP #10884) facility.
4. This report is not valid unless it bears the name of an NVLAP Lab Code 101208-0 approved signatory.
5. This report may not be used to claim product endorsement by any agency of the U.S. Government, or laboratory accrediting agency.
6. Polarized-light microscopy is not consistently reliable in detecting asbestos in floor coverings and similar nonfriable organically bound materials. Quantitative transmission electron microscopy is currently the only method that can be used to determine if this material can be considered or treated as "non-asbestos-containing.".
7. These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limitation of liability provisions. No responsibility or liability is assumed for the manner in which these results are used or interpreted.
Unless notified in writing to return the samples covered by this report, RJ Lee Group, Inc will store the samples for a period of ninety (90) days before discarding them. A shipping and handling fee will be assessed for the return of any sample.
8. This report relates only to items tested. Reproduction of this document must include all pages in order to be valid.

RJ LEE GROUP
DELIVERING SCIENTIFIC RESOLUTION

Laboratory Report

RJ Lee Group Inc.
800 Presque Isle Dr, Pittsburgh, PA 15239-2799
Tel: 724-325-1776 | Fax: 724-733-1799

	material				Cellulose			
10618300	7014F240522-09	No	2	ND	18.70%	81.30%	Carbonates, Gypsum, Misc. Particles	AD - 06/04/2024
Label: 06/04/2024 10:40					Cellulose			
Description: White and beige rocky material, brown and black paper material								
Layer Information:								
	90%-White and beige rocky material	Yes		ND	10.00%	90.00%	Carbonates, Gypsum	
					Cellulose			
	10%-Brown and black paper material	Yes		ND	97.00%	3.00%	Misc. Particles	
					Cellulose			

Authorized Signature:



Allison Durkee, Microscopist

DISCLAIMER NOTES

1. "ND" indicates no asbestos was detected.
2. "Trace" or "<" indicates asbestos was identified in the sample, but the concentration is less than the method quantitation limit.
PLM coefficients of variance range from approximately 1.8 at the quantitation limit of 0.25% to 0.32 at high fiber concentrations.
3. Sample(s) for this project were analyzed at our: Pittsburgh, PA (AIHA LAP, LLC. #292885, NY ELAP #10884) facility.
4. This report is not valid unless it bears the name of an NVLAP Lab Code 101208-0 approved signatory.
5. This report may not be used to claim product endorsement by any agency of the U.S. Government, or laboratory accrediting agency.
6. Polarized-light microscopy is not consistently reliable in detecting asbestos in floor coverings and similar nonfriable organically bound materials. Quantitative transmission electron microscopy is currently the only method that can be used to determine if this material can be considered or treated as "non-asbestos-containing.".
7. These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limitation of liability provisions. No responsibility or liability is assumed for the manner in which these results are used or interpreted. Unless notified in writing to return the samples covered by this report, RJ Lee Group, Inc will store the samples for a period of ninety (90) days before discarding them. A shipping and handling fee will be assessed for the return of any sample.
8. This report relates only to items tested. Reproduction of this document must include all pages in order to be valid.

RJ Lee Group, Inc
800 Presque Isle Dr.
Pittsburgh PA 15239
Tel: (724) 325-1776 | Fax (724) 733-1799

Final Laboratory Report

TEM Compositional Analysis

Attention: William Padgett
Savannah River Nuclear Solutions US DOE
SRNS LLC
Aiken, SC 29808
US

Report Date:	06/06/2024
Sample Receipt Date:	05/28/2024
RJ Lee Group Job No.:	COH1074798-2
Authorization/P.O. No.:	Subcontract 996
Samples Received:	6
Client Job No.:	7014F240522

Method: Chatfield Technical Consulting Limited, SOP-1988-02.Rev1.

				----------Weight Percent----------						
Client Sample Number	RJLG Sample Number	Sample Description	Starting Weight (gm)	Organic	Acid Soluble	Residue	Chry	Amph	Total Asbestos	Amphibole Type
7014F240522-01A	10618339.HT		0.24310	51	43	6	0	0	0	
7014F240522-02A	10618340.HT		0.28770	25	62	13	0	0	0	
7014F240522-03A	10618341.HT		0.20160	32	38	30	0	0	0	
7014F240522-04A	10618342.HT		0.20420	26	65	9	0	0	0	
7014F240522-05A	10618343.HT		0.24330	47	4	49	0	0	0	
7014F240522-06A	10618344.HT		0.22220	55	8	38	0	0	0	

NOTES
1. "<" indicates results less than analytical sensitivity. "---" indicates that sample was not analyzed.
2. Sample(s) for this project were analyzed at our: Pittsburgh, PA (AIHA LAP, LLC #292885, NVLAP #101208-0, NY ELAP #10884) facility.
3. If RJ Lee Group, Inc. did not collect the samples analyzed, the verifiability of the laboratory's results are limited to the reported values.
4. Trace indicates <1% asbestos was identified.
5. Abbreviations: N/A-Not Applicable, Chry-Chrysotile Asbestos, Amph-Amphibole Asbestos, Asb-Asbestos Amphibole, Cleavage-Cleavage Amphibole.
6. Samples will be held for 90 days and then disposed of per Federal regulations.
7. These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limitation of liability provisions. No responsibility or liability is assumed for the manner in which these results are used or interpreted.
8. This report relates only to items tested. Reproduction of this document must include all pages in order to be valid.

DISCLAIMER

RJ Lee Group, Inc. is accredited by the New York Department of Health Environmental Laboratory Program (NY ELAP) for the bulk analysis by TEM of non-friable organically bound materials. This report may not be used to claim product endorsement by NY ELAP, or any other regulatory or laboratory accrediting agency. Any reproduction of this document must be in full in order for the report to be valid. This report is not valid unless it bears the name of a NVLAP approved signatory.

These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limiting provisions and no responsibility or liability is assumed for the manner in which the results are used or interpreted. Unless notified in writing to return the samples covered by this report, RJ Lee Group will store the samples for a period of ninety (90) days before discarding. A shipping and handling fee will be assessed for the return of any sample.

RJ Lee Group, Inc.

Final Laboratory Report (cont'd)

RJ Lee Group Job No: COH1074798-2
Client Job No/Name: 7014F240522

Client: Savannah River Nuclear
Report Date: 06\06\2024

Authorized Signature: _____
Jon Swope, Scientist

NOTES
1. "<" indicates results less than analytical sensitivity. "---" indicates that sample was not analyzed.
2. Sample(s) for this project were analyzed at our: Pittsburgh, PA (AIHA LAP, LLC #292885, NVLAP #101208-0, NY ELAP #10884) facility.
3. If RJ Lee Group, Inc. did not collect the samples analyzed, the verifiability of the laboratory's results are limited to the reported values.
4. Trace indicates <1% asbestos was identified.
5. Abbreviations: N/A-Not Applicable, Chry-Chrysotile Asbestos, Amph-Amphibole Asbestos, Asb-Asbestos Amphibole, Cleavage-Cleavage Amphibole.
6. Samples will be held for 90 days and then disposed of per Federal regulations.
7. These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limitation of liability provisions. No responsibility or liability is assumed for the manner in which these results are used or interpreted.
8. This report relates only to items tested. Reproduction of this document must include all pages in order to be valid.

DISCLAIMER

RJ Lee Group, Inc. is accredited by the New York Department of Health Environmental Laboratory Program (NY ELAP) for the bulk analysis by TEM of non-friable organically bound materials. This report may not be used to claim product endorsement by NY ELAP, or any other regulatory or laboratory accrediting agency. Any reproduction of this document must be in full in order for the report to be valid. This report is not valid unless it bears the name of a NVLAP approved signatory.

These results are submitted pursuant to RJ Lee Group's current terms and conditions of sale, including the company's standard warranty and limiting provisions and no responsibility or liability is assumed for the manner in which the results are used or interpreted. Unless notified in writing to return the samples covered by this report, RJ Lee Group will store the samples for a period of ninety (90) days before discarding. A shipping and handling fee will be assessed for the return of any sample.

COH1074798-0
COH1074798-2

COPY

SRS Chain of Custody / Laboratory Analysis Request

Requested TAT: ☐ Rush ☒ Routine ☐ Other

Activity Code: 0L2NENGDSN

Samples received in good condition? ☐ Y ☐ N

Lab Name	R J Lee Group, Inc Sample Management Department
Address 1	800 Presque Isle Drive
Address	Pittsburgh, PA 15239
POC	Monica McGrath-Koerner 724-387-1959 Ashleigh Sload 724-387-1936

Sample Comments

Use positive stop for all homogeneous groups. Negative results for non-friable organically bound (NOB) shall be verified with at least one TEM analysis.

Peer Reviewed / Self Check by

Name (Print): CARLOS SANTOS

Return Results / Electronic Report To

Name (CTF)	William Padgett
Email / Phone	Ken.Padgett@srs.gov (803) 952-5650
Name (STR)	William Padgett
Email / Phone	Ken.Padgett@srs.gov (803) 952-5650
Name (Req by)	James Moore
Email / Phone	James.moore@srs.gov/ 803-952-6439
Organization	EC-ACP
Address	Savannah River Site Aiken, SC 29802

This Line Laboratory use ONLY	Laboratory ID#:	Results attached (date):	Results Pages (Total)

No	Field ID	Matrix	Sample Date / Time	Requested Analysis	Sample Media / Size	Time (min)	Vol / Area	Sample Comments
	7014F240522-01A		05/22/24	TEM	< 1 Gram	N/A	N/A	H01OB-White elastomer (exterior)
	7014F240522-02A		05/22/24	TEM	< 1 Gram	N/A	N/A	H02OB-12x12 Tan/white speck floor tile
	7014F240522-03A		05/22/24	TEM	< 1 Gram	N/A	N/A	H03OB-Adhesive on 3" cove base molding
	7014F240522-04A		05/22/24	TEM	< 1 Gram	N/A	N/A	H04OB-Interior: caulk around windows & doors
	7014F240522-05A		05/22/24	TEM	< 1 Gram	N/A	N/A	H05OB-Red putty around upper piping
	7014F240522-06A		05/22/24	TEM	< 1 Gram	N/A	N/A	H06OB-Blue putty on penetrations
	7014F240522-07		05/22/24	PLM	< 1 Gram	N/A	N/A	H07-Gypsumboard above ceiling tile
	7014F240522-08		05/22/24	PLM	< 1 Gram	N/A	N/A	H07-Gypsumboard above ceiling tile
	7014F240522-09		05/22/24	PLM	< 1 Gram	N/A	N/A	H07-Gypsumboard above ceiling tile

Relinquished by		
Name	Signature	Date and Time
James Moore		5-23-24 0645
B. Boehnke		5-23-24 0900

Received by		
Name	Signature:	Date and Time
B. Boehnke		5-23-24 0645
Fedex		52324 0900
ACiaramella		05/28/24 11:08AM

Page 1 of 1
